



MEMORANDUM

TO: Anthony Marino, Town Manager
Steven Calla, Director of Public Works

FROM: Gregory McNeal, Woodard & Curran

DATE: August 10, 2023

RE: Revere, Crest, Grovers Watermain Improvements
Two-Week Look Ahead: Anticipated Schedule

The following is a summary of the work completed this week and the work J.P. Cardillo & Son, Inc. (contractor) has scheduled for the next two weeks. Please note, the anticipated schedule may vary due to unforeseen site conditions, weather conditions, or other factors out of the contractor's control.

Construction Updates and Schedule:

Work completed this week (8/7/23 to 8/10/23):

1. Completed installation of interconnection and valves at Golden Drive.
2. Started work for installation of interconnection and valves at Sagamore Avenue.

Two-week Anticipated Schedule (8/11/23 to 8/25/23):

1. August 14 to August 18, 2023:
 - a. Scheduled Work:
 - i. Installation of 8-inch and 6-inch main, valves and hydrant at the intersection of Summit Avenue. This work will continue through the weekend.
 - ii. Installation of hydrant on Revere Street near Almont Street.
 - iii. Installation of 12-inch main and valves at intersection of Shirley Street and Revere Street.
 - b. Traffic Management:
 - i. **(M-S, 7:30 AM to 5 PM):** Portion of Revere Street will be one-way traffic adjacent to the working area. Police will direct traffic.
2. August 21 to August 25, 2023:
 - a. Scheduled Work:
 - i. Installation of 20-inch main and hydrant at intersection of Shirley Street and Revere Street.
 - ii. Installation of 8-inch main, valves and hydrant at the intersection of Shirley Street and Revere Street.
 - iii. Installation of hydrant on Summit Ave.
 - b. Traffic Management:
 - i. **(M-F, 7:30 AM to 5 PM):** Portions of Revere Street will be one-way traffic adjacent to the working area. Police will direct traffic.
 - ii.

CONSTRUCTION PHOTOS:



Photo 1: Water main construction at Golden Drive.



Photo 2: New gate valves installed at Golden Drive.

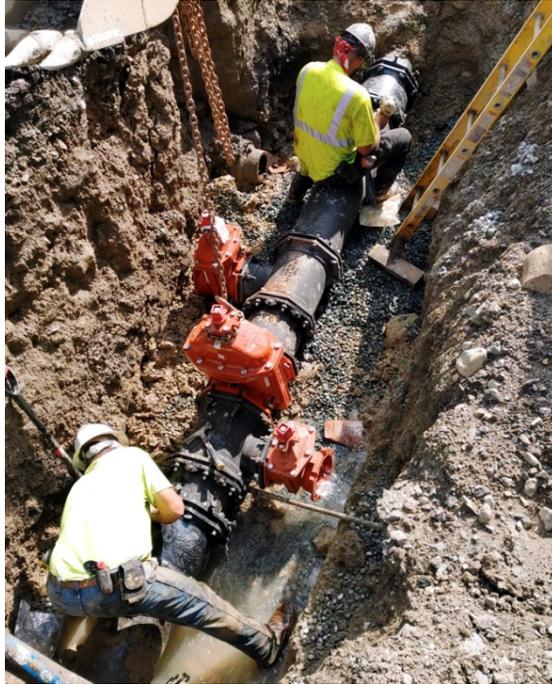


Photo 3: New gate valves installed at Sagamore Avenue.



Photo 4: New water main installed at Golden Drive.
