



MEMORANDUM

TO: Anthony Marino, Town Manager
Steven Calla, Director of Public Works

FROM: Gregory McNeal, Woodard & Curran

DATE: August 18, 2023

RE: Revere, Crest, Grovers Watermain Improvements
Two-Week Look Ahead: Anticipated Schedule

The following is a summary of the work completed this week and the work J.P. Cardillo & Son, Inc. (contractor) has scheduled for the next two weeks. Please note, the anticipated schedule may vary due to unforeseen site conditions, weather conditions, or other factors out of the contractor's control.

Construction Updates and Schedule:

Work completed this week (8/14/23 to 8/17/23):

1. Installed hydrant on Summit Ave.
2. Installation of interconnection between Revere Street and Shirley Street.

Two-week Anticipated Schedule (8/21/23 to 9/1/23):

1. August 21 to August 25, 2023:
 - a. Scheduled Work:
 - i. Complete the work for interconnection between Revere Street and Shirley Street.
 - ii. Install hydrant on Revere Street near Summit Ave, connected to the 20-inch main.
 - iii. Install hydrant on Harvard Street, and remove existing hydrant.
 - iv. Install interconnection between Revere Street and Governor's Drive.
 - b. Traffic Management:
 - i. **(M-S, 7:30 AM to 5 PM):** Portion of Revere Street will be one-way traffic adjacent to the working area. Police will direct traffic.
2. August 28 to September 1, 2023:
 - a. Scheduled Work:
 - i. Install hydrant at intersection of Revere Street and Kennedy Street.
 - ii. Install interconnection between Revere Street and Argyle Street.
 - b. Traffic Management:
 - i. **(M-F, 7:30 AM to 5 PM):** Portions of Revere Street will be one-way traffic adjacent to the working area. Police will direct traffic.

CONSTRUCTION PHOTOS:



Photo 1: Interconnection between Revere Street and Shirley Street.

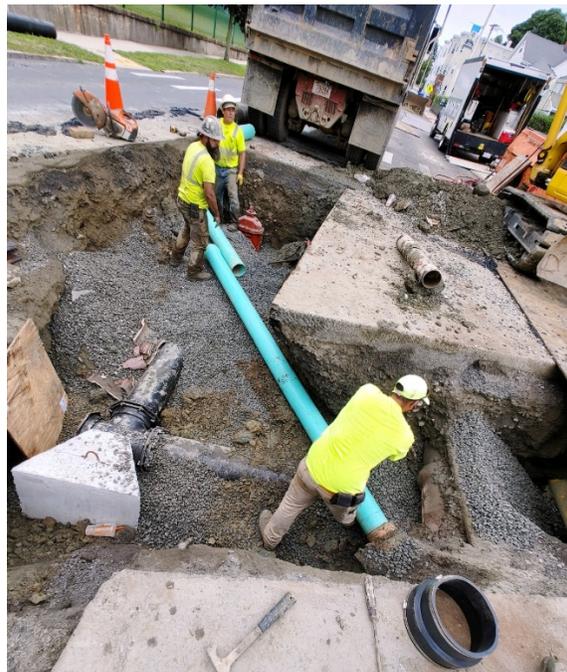


Photo 2: Interconnection between Revere Street and Shirley Street.



Photo 3: New hydrant on Summit Ave.



Photo 4: New hydrant on Summit Ave.
