



MEMORANDUM

TO: Anthony Marino, Town Manager
Steven Calla, Director of Public Works

FROM: Gregory McNeal, Woodard & Curran

DATE: September 18, 2023

RE: Revere, Crest, Grovers Watermain Improvements
Two-Week Look Ahead: Anticipated Schedule

The following is a summary of the work completed this week and the work J.P. Cardillo & Son, Inc. (contractor) has scheduled for the next two weeks. Please note, the anticipated schedule may vary due to unforeseen site conditions, weather conditions, or other factors out of the contractor's control.

Construction Updates and Schedule:

Work completed this week (9/5/23 to 9/18/23):

1. Installed approximately 600 linear feet of 15" HDPE drainage pipe on Crest Ave.
2. Installed 6 catch basins on Crest Avenue.
1. September 18 to September 22, 2023:
 - a. Scheduled Work:
 - i. Finish installing new drainage pipe and structures on Crest Avenue.
 - ii. Demotion of existing buried bridge abutment at the intersection of Crest Avenue and Revere Street.
 - iii. Connection of watermain between Crest Avenue and Revere Street.
 - iv. Remove and reset granite curbs, and install new sidewalks on Grovers Avenue.
 - b. Traffic Management:
 - i. **(M-F 2PM to 5 AM):** Portions of Crest Avenue will be closed to through traffic in the vicinity of the work area. Police will direct traffic.
2. September 25 to September 29, 2023:
 - a. Scheduled Work:
 - i. Remove and reset granite curbs, and install new sidewalks on Grovers Avenue.
 - ii. Install watermain connections at Argyle Street and Highland Avenue.
 - b. Traffic Management:
 - i. **(M-F 2PM to 5 AM):** Portions of Revere Street will be one-way traffic in the vicinity of the work area. Police will direct traffic.

CONSTRUCTION PHOTOS:



Photo 1: Trench preparation for drain line installation on Crest Avenue.

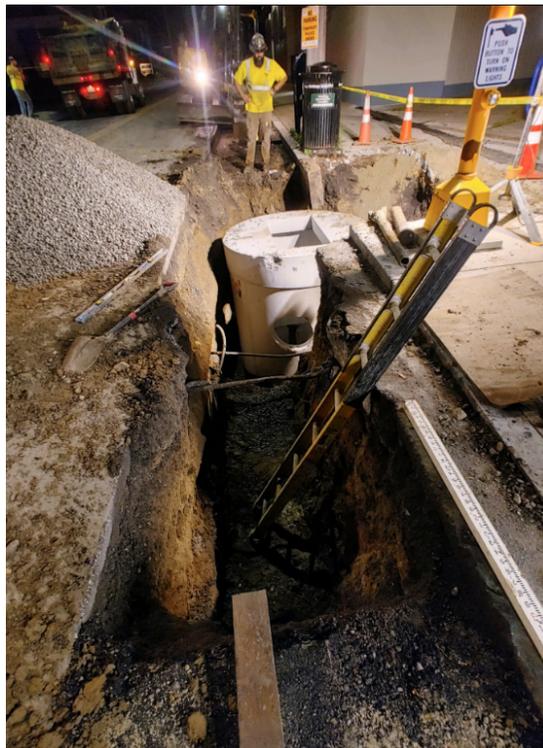


Photo 2: Installing new drainage structure on Crest Avenue.



Photo 3: Installing new drain pipe and structure on Crest Avenue.



Photo 4: Setting new and existing drain pipes into new drainage structure on Crest Avenue.
